



CITY OF
**PALO
ALTO**

Palo Alto Fire Station #4



MONTHLY REPORT 04

APRIL 2026

PREPARED BY CUMMING GROUP

Project Information

Fire Station #4

City of Palo Alto

Brown Reynolds Watford
Architects

Architect

Beals Martin
General Contractor

Cumming Group
Project Manager

Fire Station No. 4 was built in 1953 and located at 3600 Middlefield Road. The existing fire station building does not serve the current needs of the Fire Department and does not effectively use the current 0.6-acre portion of the property. City Council included the replacement of Fire Station No. 4 in the Infrastructure Plan approved in June 2014. This project will provide a new facility built to current essential services standards with a high likelihood of being fully operational during and after a major disaster such as a significant earthquake.

Beals Martin was awarded the construction contract on October 20, 2025. Construction began on December 1, 2025, with building abatement finished on December 11, 2025 and deconstruction completed on January 7, 2026. Site work began on January 16, 2026 and construction is anticipated to be completed June 2027.




Activities

Recently Completed Activities

- Stripped concrete wall forms
- Underground plumbing installation
- Underground plumbing inspection

Upcoming Activities

- Under slab electrical installation and inspection
- Vapor barrier installation
- Set trench drains
- Slab rebar installation and concrete pour

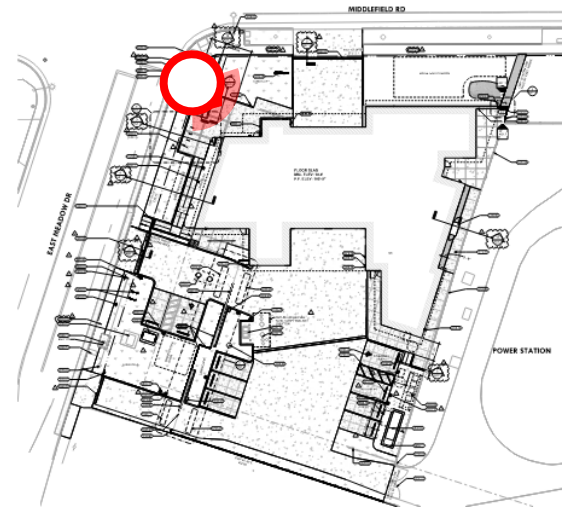

Project Photos



Completed concrete shear walls

Project Photos



Site progression
