



CITY OF
**PALO
ALTO**

Palo Alto Fire Station #4



MONTHLY REPORT 06

JUNE 2026

PREPARED BY CUMMING GROUP

Project Information

Fire Station #4

City of Palo Alto

Brown Reynolds Watford
Architects

Architect

Beals Martin
General Contractor

Cumming Group
Project Manager

Fire Station No. 4 was built in 1953 and located at 3600 Middlefield Road. The existing fire station building does not serve the current needs of the Fire Department and does not effectively use the current 0.6-acre portion of the property. City Council included the replacement of Fire Station No. 4 in the Infrastructure Plan approved in June 2014. This project will provide a new facility built to current essential services standards with a high likelihood of being fully operational during and after a major disaster such as a significant earthquake.

Beals Martin was awarded the construction contract on October 20, 2025. Construction began on December 1, 2025, with building abatement finished on December 11, 2025 and deconstruction completed on January 7, 2026. Site work began on January 16, 2026 and construction is anticipated to be completed June 2027.




Activities

Recently Completed Activities

- Completion of site electrical work and electrical inspections
- Installation of slab protection
- Steel erection and base plate grouting
- Roof pan decking installation

Upcoming Activities

- Temporary power relocation
- Exterior metal stud installation
- Roof curb and roof hatch installation
- Soffit framing and gutters
- Exterior wall mockup installation, inspections, and testing

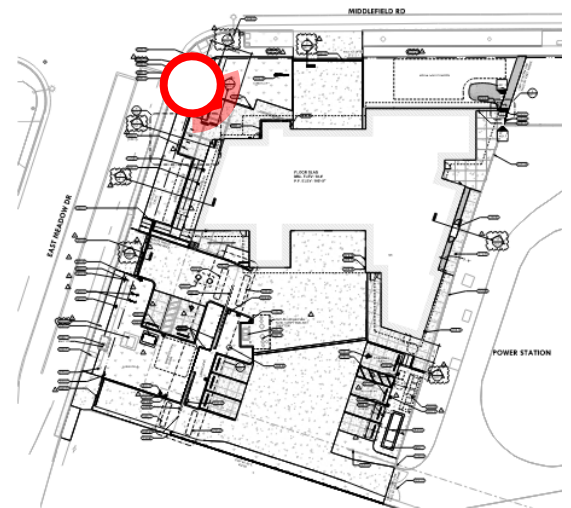

Project Photos



Trench and electrical conduits



Slab protection

Project Photos



Steel erection
